



OFFICE OF THE WATERFRONT

January 12, 2016

ALASKAN WAY VIADUCT REPLACEMENT PROGRAM
STAKEHOLDER GROUP

2015 WORK PLAN: KEY ACCOMPLISHMENTS

- Completed MarketFront (PC-1 North) Development Agreement *(May)*
- Completed Draft Environmental Impact Statement (EIS) for Alaskan Way, Promenade and Overlook Walk *(June)*
- Aquarium Master Plan approved by Council *(August)*
- Maintenance Report completed *(November)*
- Design progress on critical utilities, including telecommunications, Seattle City Light and Seattle Public Utilities and Puget Sound Energy coordination *(30% designs completed, continues in 2016)*
- Continued stakeholder engagement *(ongoing)*

NEXT STEPS IN 2016



- Supplement Draft EIS for Alaskan Way, Promenade and Overlook Walk (*spring*)
- Develop MOU with Aquarium regarding next steps for expansion (*summer*)
- Complete updated 60% design of Main Corridor (*summer*)
- Final EIS for Alaskan Way, Promenade and Overlook Walk (*fall*)
- Cost Estimate and Validation Process (CEVP) workshop with WSDOT (*fall*)
- Complete City/WSDOT funding agreement (*end of year*)


SUPPLEMENTAL DRAFT EIS



- OW will complete a Supplemental Draft EIS in spring 2016
- Final EIS is anticipated in fall 2016
- In addition to the action and no action alternatives evaluated in the Draft EIS, the Supplemental Draft EIS will evaluate two new alternatives:
 - A narrower Alaskan Way that does not include dedicated bus lanes between Yesler and King streets (transit would operate in the general purpose lanes)
 - A revised Overlook Walk to accommodate a potential Aquarium expansion project in that location



SCHEDULE

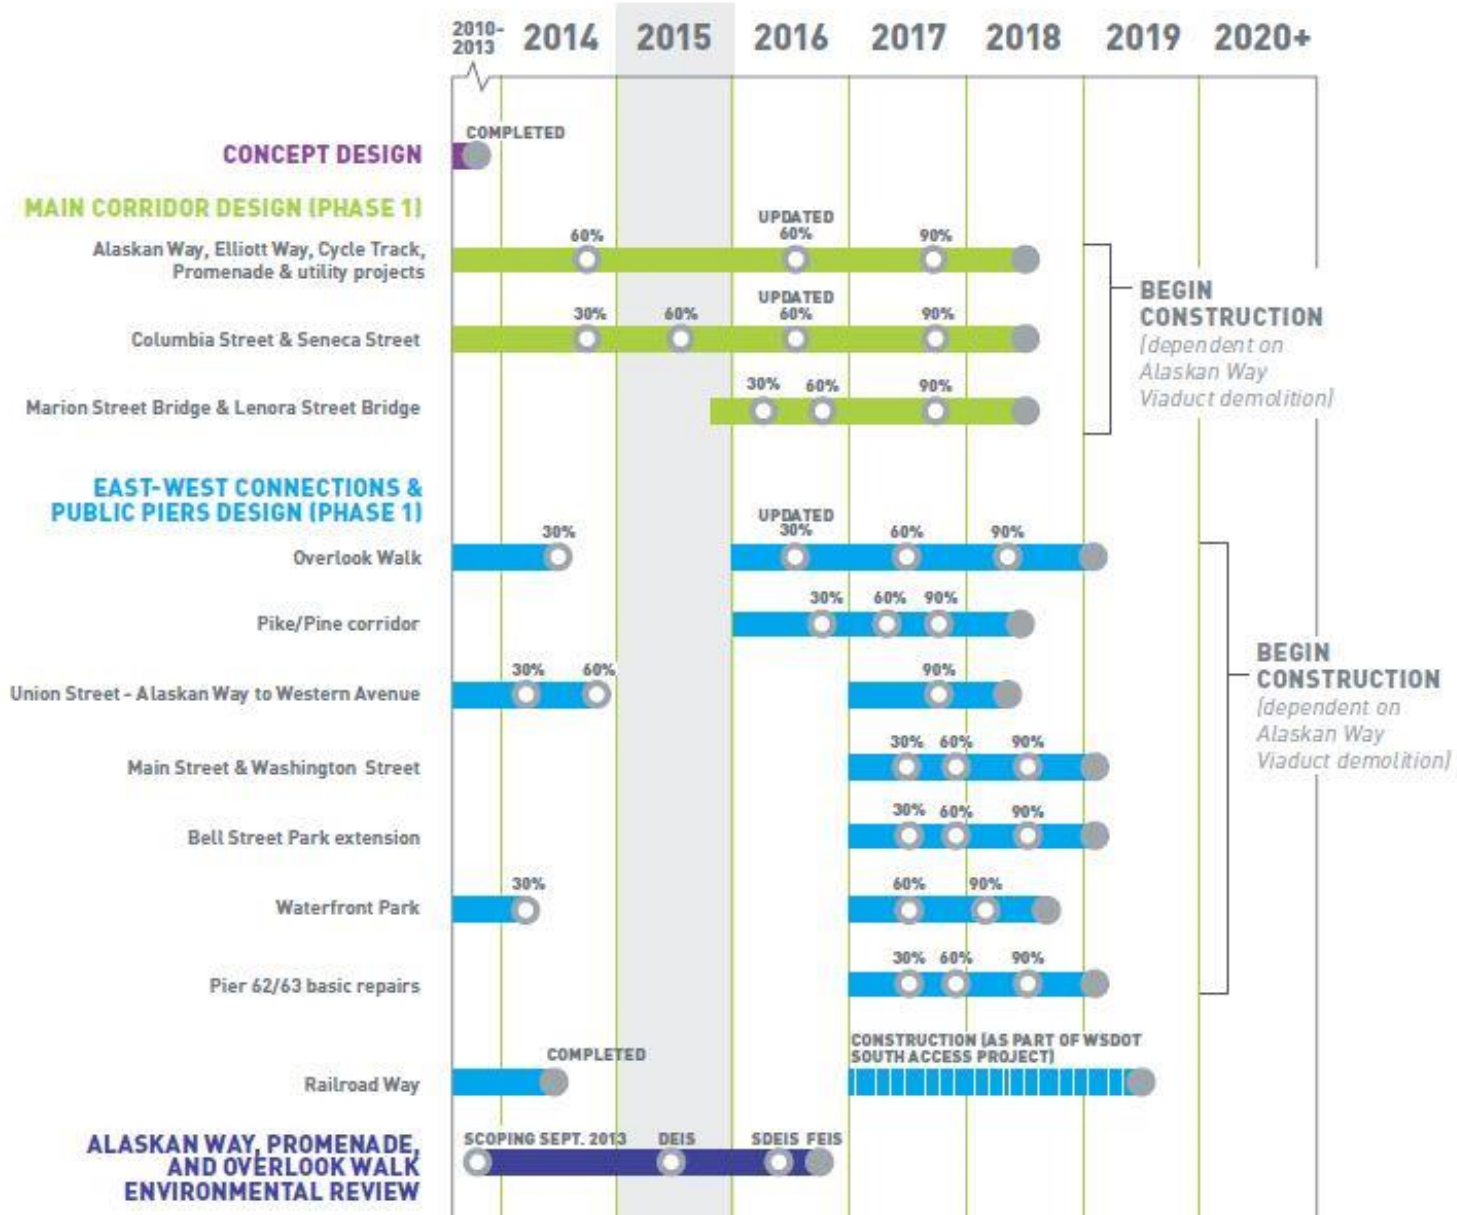



QUESTIONS?
